

						نموذج تقديم اعتماد مواد					
تاريخ نهاية العقد			1.375.641.5			قيمة العقد			توريد وتركيب وتشغيل أنظمة الإطفاء وإنذار الحريق لأحد المواقع التابعة لديوان رئاسة أمن الدولة بحافظة الطائف		
باسكو سيفتي			المقاول			مكتب نسج الابداع للاستشارات الهندسية			الاستشاري		
رئاسة أمن الدولة			المالك			الطائف			موقع المشروع		
بيانات التقديم											
رقم التقديم			MAS-MECH-10-R01			تاريخ التقديم			12/05/2026		
التصنيف			معماري			كهرباء			ميكانيكا		
نوع التقديم			مستند			مواد			مخططات		
الكود			الوصف			التسلسل			الكود		
10			Alarm Check Valve.			1			12		
11			Size: 6" (150 mm).			2			12		
12			Supplier: Mechanical Future (مستقبل الميكانيكا). Certification: UL Listed / FM Approved			3			12		
الاستلام			المقاول			Model: ZSFZ8X9			4		
الختم			التوقيع			ممثل المقاول			5		
6			7			8			9		
12/05/2026 م 25/11/1447 هـ			م - احمد علي مصطفى			12/05/2026 م 25/11/1447 هـ			12/05/2026 م 25/11/1447 هـ		
المراجعة الفنية			الملاحظات الفنية								
المدني / الانشائي			المدني / الانشائي								
المعماري			المعماري								
الكهربائي			الكهربائي								
الميكانيكي			الميكانيكي								
مدير المشروع			مدير المشروع								
التوقيع			التوقيع								
التاريخ			التاريخ								
مقبول			مقبول			مقبول			مقبول		
مقبول حسب الملاحظات: B			مقبول			مقبول			مقبول		
مرفوض وبعاد التقديم: C			مقبول			مقبول			مقبول		
يتعهد المقاول المذكور أعلاه بأنه قد راجع كافة تفاصيل التقديم وطابقها مع شروط ومواصفات ومخططات المشروع المعتمدة وأن هذه الموافقة لا تخلي مسؤوليته حسب متطلبات العقد											

				نموذج تقديم اعتماد مواد			
تاريخ نهاية العقد		1.375.641.5		قيمة العقد		توريد وتركيب وتشغيل أنظمة الإطفاء و انذار الحريق لأحد المواقع التابعة لديوان رئاسة أمن الدولة بحافظة الطائف	
باسكو سبكي		المقاول		مكتب نسج الابداع للاستشارات الهندسية		رئاسة أمن الدولة	
المالك		الطائف		موقع المشروع		التايف	
بيانات التقديم							
رقم التقديم		MAS-MECH-10-R00		تاريخ التقديم		29/04/2026	
التصنيف		ميكانيكا		نوع التقديم		مستند	
التوصيل		الكود		الوصف		الكود	
1		Alarm Check Valve		10		الوصف	
2		Size: 6" (150 mm)		11		الكود	
3		Supplier: Mechanical Future (مستقبل الميكانيكا). Certification: UL Listed / FM Approved.		12		الكود	
4		Model: ZSFZ8X9		الاستلام		المقاول	
5		الختم		التوقيع		ممثل المقاول	
6		29/04/2026 م 12/11/1447 هـ		التاريخ		م- احمد علي مصطفى	
7		29/04/2026 م 12/11/1447 هـ		التاريخ		م- احمد علي مصطفى	
8		29/04/2026 م 12/11/1447 هـ		التاريخ		م- احمد علي مصطفى	
9		29/04/2026 م 12/11/1447 هـ		التاريخ		م- احمد علي مصطفى	
المراجعة الفنية				الملاحظات الفنية			
المديني / الانشائي				يجب ارفاق شهادات الاعتماد (UL and FM) المذكورة بالكتالوج المرفقة أدناه			
المعماري				الملاحظات الفنية			
الكهربائي				الملاحظات الفنية			
الميكانيكي				الملاحظات الفنية			
مدير المشروع				الملاحظات الفنية			
التوقيع				الملاحظات الفنية			
التاريخ				الملاحظات الفنية			
9/5/2026				الملاحظات الفنية			
مرفوض ويعاد التقديم: C				مقبول حسب الملاحظات: B			
مقبول: A				الكود			
العدد				المرفقات			
5				التاريخ			
ممثل المالك				التاريخ			

يتعهد المقاول المذكور أعلاه بأنه قد راجع كافة تفاصيل التقديم وطايقها مع شروط ومواصفات ومخططات المشروع المعتمدة وأن هذه الموافقة لا تخلي مسؤوليته حسب متطلبات العقد

GROOVED WET ALARM CHECK VALVE

Type: ZSFZ8X9

Doc No: DS-901-ZSFZ8X9-01-E-X

1.0 PRODUCT OVERVIEW

The alarm check valve works as a check valve by preventing the reverse flow of water from the system piping to the water supply. The valve is trimmed with a water bypass line, which has an in-line swing check valve. The bypass line allows pressure surges to enter the system and to be trapped above the alarm check valve's clapper without the clapper lifting and causing false alarms.

When significant flow of water occurs, such as from an open sprinkler, the alarm valve's clapper lifts and allows water to enter the system. Simultaneously, water enters an intermediate chamber, which allows the water to activate an alarm either through a water motor alarm or through a water pressure alarm. These alarms continue to sound until the flow of water is stopped.



Dimensions:

3"(DN80)-8"(DN200)

Design Standard:

UL 193, ULC-ORD-C193, FM1041, GB 5135.2

Connection Standard:

ISO 6182, AWWA C606

Working Pressure:

PN16/PN10, 300PSI, 250PSI, 200PSI

Application:

The wet alarm valve is an important component of the wet sprinkler system. The

Sign Off:

Owner: _____ Contractor: _____ Engineer: _____
Location: _____ Date: _____ Approved & Date: _____

operating temperature range is 0°C-80°C.

Pipe Material:

Welded and seamlessly rolled steel pipe:

ASME B36.10、ASTM A53-A53M、ISO 4200、GB/T 21835-2008

Grooved Coupling: ISO6182、GB 5135.11、AWWA C606

Surface Treatment:


- ☐RAL3000 painting
- ☐RAL3000 Epoxy power painting
- ☐HS-1701B
- ☐Others would be available upon clients' detailed request

2.0 APPROVALS



3.0 SPECIFICATIONS

Product Sketch:

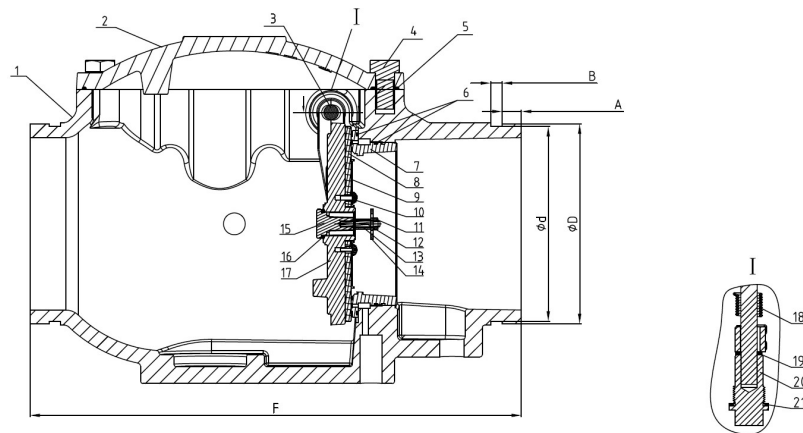


Part No.	Part	Standard Specification	Options
1	Valve Body	ASTM A536 65-45-12	
2	Bonnet	ASTM A536 65-45-12	
3	Pin	AISI 304	

Sign Off:

Owner: _____ Contractor: _____ Engineer: _____
 Location: _____ Date: _____ Approved & Date: _____

4	Hex Bolt	Carbon Steel Zinc Plated	
5	Gasket	EPDM	
6	O-Ring	NBR	
7	Seat	C89833	
8	Gasket	EPDM	
9	Plate	AISI 304	
10	Hex Nut	AISI304	
11	Hex Nut	AISI304	
12	Adjustment Screw	AISI304	
13	Core Tube	AISI304	
14	Core Board	AISI304	
15	Disc Core	C89833	
16	O-Ring	NBR	
17	Disc	C89833	
18	Spring	AISI304	
19	Plug Gasket	PTFE	
20	Plug	AISI304	
21	Plug Gasket	PTFE	

External Accessories

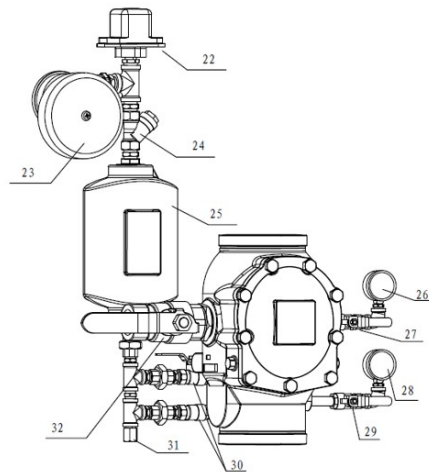

External Accessories			
Part No	Part	Part No	Part
22	Pressure Switch	28	Pressure Switch
23	Alarm	29	Ball Valve
24	Strainer	30	Ball Valve

Sign Off:

Owner: _____ Contractor: _____ Engineer: _____

Location: _____ Date: _____ Approved & Date: _____


25	Decelerator	31	Throttle valve
26	Pressure Switch	32	Ball Valve
27	Ball Valve		

4.0 DIMENSIONS AND PERFORMANCE

4.1 Dimensions

Size		Dimensions					
in	DN	OD	A	B	Φ d	Φ D	F
3"	80	88.9	15.88	7.93	84.94	88.9	320.3
4"	100	114.3	15.88	9.53	110.08	114.3	382
6"	150	159.0	15.88	9.53	154.5	159.0	406.4
		165.1	15.88	9.53	160.9	165.1	406.4
		168.3	15.88	9.53	163.96	168.3	406.4
8"	200	219.1	19.05	11.1	214.4	219.1	446

4.2 Flow rates

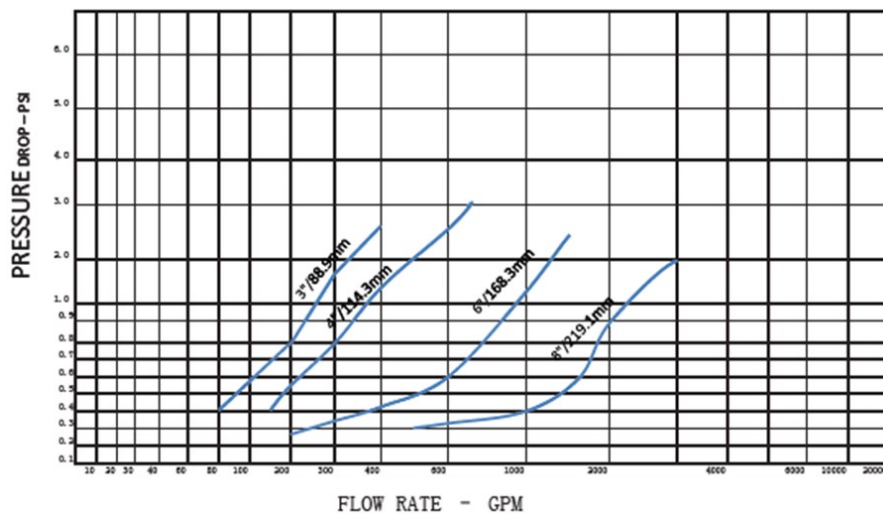

4.3.1. Shell Body Test

Disc assembly, 2 times rated working pressure

Decelerator, 2 times rated working pressure

4.3.2. Leakage Test

Wet disc valve system side and connecting pipe fittings, 2 times rated working pressure

times the rated working pressure when the disc assembly in the open position

4.3.3. Alarm function

When the inlet pressure is 0.14MPa and the system side discharge flow is 15 L/min, neither the pressure switch nor the hydraulic alarm can issue an alarm

Sign Off:

Owner: _____ Contractor: _____ Engineer: _____
 Location: _____ Date: _____ Approved & Date: _____

signal.

The inlet pressure is 0.14MPa, 0.70 MPa, 1.20 MPa, 1.60 MPa, the corresponding side discharge flow of the system side is 60 L/min, 80 L/min, 170 L/min, 170 L/min, pressure switch and hydraulic alarm The bells must issue an alarm signal.

Delay adjustment time: The alarm device starts to issue a continuous alarm within 5s-90s after the system side releases water.

5.0REFERENCE MATERIALS

Approved certification for Grooved Wet Alarm Check Valve

Sign Off:

Owner:_____ Contractor:_____ Engineer: _____
Location:_____ Date:_____ Approved& Date: _____

GROOVED WET ALARM CHECK VALVE

Type: ZSFZ8X9

Doc No: DS-901-ZSFZ8X9-01-E-X

1.0 PRODUCT OVERVIEW

The alarm check valve works as a check valve by preventing the reverse flow of water from the system piping to the water supply. The valve is trimmed with a water bypass line, which has an in-line swing check valve. The bypass line allows pressure surges to enter the system and to be trapped above the alarm check valve's clapper without the clapper lifting and causing false alarms.

When significant flow of water occurs, such as from an open sprinkler, the alarm valve's clapper lifts and allows water to enter the system. Simultaneously, water enters an intermediate chamber, which allows the water to activate an alarm either through a water motor alarm or through a water pressure alarm. These alarms continue to sound until the flow of water is stopped.



Dimensions:

3"(DN80)-8"(DN200)

Design Standard:

UL 193, ULC-ORD-C193, FM1041, GB 5135.2

Connection Standard:

ISO 6182, AWWA C606

Working Pressure:

PN16/PN10, 300PSI, 250PSI, 200PSI

Application:

The wet alarm valve is an important component of the wet sprinkler system. The

Sign Off:

Owner: _____ Contractor: _____ Engineer: _____
Location: _____ Date: _____ Approved & Date: _____

operating temperature range is 0°C-80°C.

Pipe Material:

Welded and seamlessly rolled steel pipe:

ASME B36.10、ASTM A53-A53M、ISO 4200、GB/T 21835-2008

Grooved Coupling: ISO6182、GB 5135.11、AWWA C606

Surface Treatment:


- ☐RAL3000 painting
- ☐RAL3000 Epoxy power painting
- ☐HS-1701B
- ☐Others would be available upon clients' detailed request

2.0 APPROVALS



3.0 SPECIFICATIONS

Product Sketch:

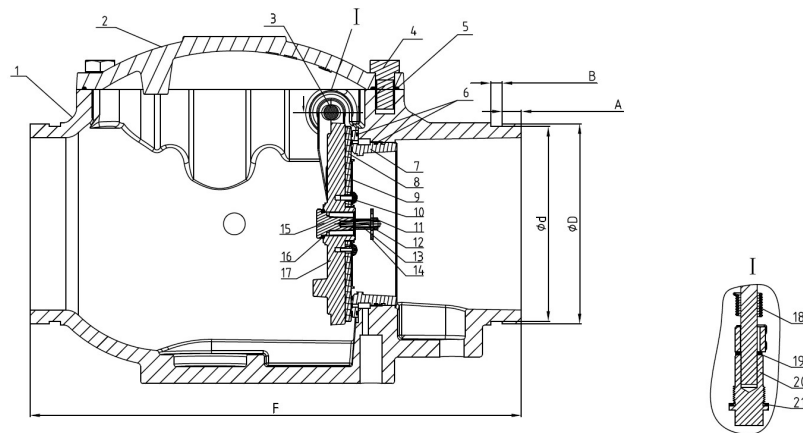


Part No.	Part	Standard Specification	Options
1	Valve Body	ASTM A536 65-45-12	
2	Bonnet	ASTM A536 65-45-12	
3	Pin	AISI 304	

Sign Off:

Owner: _____ Contractor: _____ Engineer: _____
 Location: _____ Date: _____ Approved & Date: _____

4	Hex Bolt	Carbon Steel Zinc Plated	
5	Gasket	EPDM	
6	O-Ring	NBR	
7	Seat	C89833	
8	Gasket	EPDM	
9	Plate	AISI 304	
10	Hex Nut	AISI304	
11	Hex Nut	AISI304	
12	Adjustment Screw	AISI304	
13	Core Tube	AISI304	
14	Core Board	AISI304	
15	Disc Core	C89833	
16	O-Ring	NBR	
17	Disc	C89833	
18	Spring	AISI304	
19	Plug Gasket	PTFE	
20	Plug	AISI304	
21	Plug Gasket	PTFE	

External Accessories

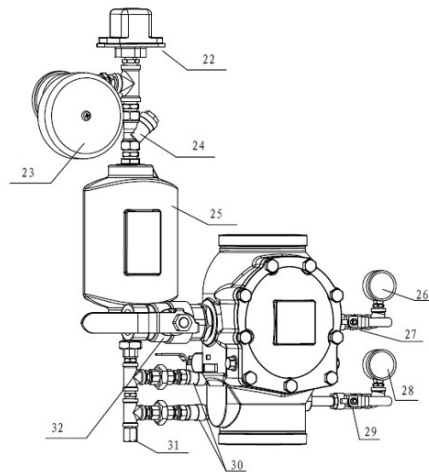

External Accessories			
Part No	Part	Part No	Part
22	Pressure Switch	28	Pressure Switch
23	Alarm	29	Ball Valve
24	Strainer	30	Ball Valve

Sign Off:

Owner: _____ Contractor: _____ Engineer: _____

Location: _____ Date: _____ Approved & Date: _____


25	Decelerator	31	Throttle valve
26	Pressure Switch	32	Ball Valve
27	Ball Valve		

4.0 DIMENSIONS AND PERFORMANCE

4.1 Dimensions

Size		Dimensions					
in	DN	OD	A	B	Φ d	Φ D	F
3"	80	88.9	15.88	7.93	84.94	88.9	320.3
4"	100	114.3	15.88	9.53	110.08	114.3	382
6"	150	159.0	15.88	9.53	154.5	159.0	406.4
		165.1	15.88	9.53	160.9	165.1	406.4
		168.3	15.88	9.53	163.96	168.3	406.4
8"	200	219.1	19.05	11.1	214.4	219.1	446

4.2 Flow rates

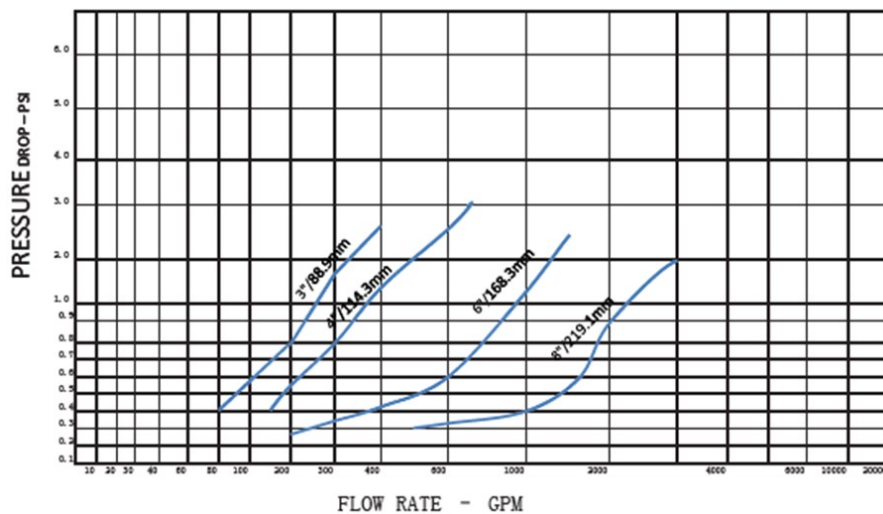

4.3.1. Shell Body Test

Disc assembly, 2 times rated working pressure

Decelerator, 2 times rated working pressure

4.3.2. Leakage Test

Wet disc valve system side and connecting pipe fittings, 2 times rated working pressure

times the rated working pressure when the disc assembly in the open position

4.3.3. Alarm function

When the inlet pressure is 0.14MPa and the system side discharge flow is 15 L/min, neither the pressure switch nor the hydraulic alarm can issue an alarm

Sign Off:

Owner: _____ Contractor: _____ Engineer: _____
 Location: _____ Date: _____ Approved & Date: _____

signal.

The inlet pressure is 0.14MPa, 0.70 MPa, 1.20 MPa, 1.60 MPa, the corresponding side discharge flow of the system side is 60 L/min, 80 L/min, 170 L/min, 170 L/min, pressure switch and hydraulic alarm The bells must issue an alarm signal.

Delay adjustment time: The alarm device starts to issue a continuous alarm within 5s-90s after the system side releases water.

5.0 REFERENCE MATERIALS

Approved certification for Grooved Wet Alarm Check Valve

Sign Off:

Owner: _____ Contractor: _____ Engineer: _____
Location: _____ Date: _____ Approved & Date: _____



Sprinkler System Components | Water Motor Gongs | **Waterflow Alarm System Valves**

Model ZSFZ8X9

Product Description

Model No	Description	Valve Size		Rated Working Pressure		End Connection	Remarks
		in	(mm)	psi	(kPa)		
ZSFZ8X9	Alarm Check Valve	3 , 4 , 6 , 8	(80, 100, 150, 200)	300	(2065)	Grooved x Grooved	a, b
ZSFZ8X9	Alarm Check Valve		88.9, 114.3, 159, 165.1, 168.3, 219.1	300	(2065)	Grooved x Grooved	a, b

Remarks:

- a. Resilient seat.
- b. FM Approved for Vertical Installations Only

Details

Category	Waterflow Alarm System Valves
Class of Work	1041 - Alarm Check Valves
Approval Standard	FM 1041 - Alarm Check Valves
Certification Type	FM Approved
Listing Country	China

Company

Jinan Meide Casting Co Ltd
No.1 Meide Street, Meigui Town,
Pingyin County, Jinan City, China
<http://meide-casting.com>

Model ZSFZ8X9

File Number: EX26840

COMPANY

JINAN MEIDE CASTING CO LTD

Meide Science And Technology Park
Pingyin Industrial Park
Jinan, Shandong 250400 China

MODEL INFO

ZSFZ8X9

Alarm Valve

PRODUCT INFORMATION

Body Type	Nom Pipe Size, NPS	End Configuration	Max Rated Pressure, psig (kPa)	Supply Pressure Type	Alarm Device Type	Alarm Device Model	Retard Chamber Model	Installed Position
Globe	3, 4, 6, 165.1 mm, 8	Groove	300 (2068)	Variable	Water motor gong	NX010	YSQ	Vertical
Globe	3, 4, 6, 165.1 mm, 8	Groove	300 (2068)	Variable	Electric pressure switch	UL Listed (VOXZ)	YSQ	Vertical
Globe	3, 4, 6, 165.1 mm, 8	Groove	300 (2068)	Constant	Water motor gong	NX010	Not Applicable	Vertical
Globe	3, 4, 6, 165.1 mm, 8	Groove	300 (2068)	Constant	Electric pressure switch	UL Listed (VOXZ)	Not Applicable	Vertical

GENERAL

Installation Limitations

End configurations are intended to be installed on systems not exceeding end configurations' working capabilities.

UL Solutions permits the reproduction of the material contained in Product iQ subject to the following conditions: 1. The Guide Information, Assemblies, Constructions, Designs, Systems, and/or Certifications (files) must be presented in their entirety and in a non-misleading manner, without any manipulation of the data (or drawings). 2. The statement "Reprinted from Product iQ with permission from UL Solutions" must appear adjacent to the extracted material. In addition, the reprinted material must include a copyright notice in the following format: "©2026 UL LLC."
